


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Calendar
1	★	Notice to Proceed/Paving Schedule	179 days	Wed 7/15/20	Mon 3/22/21			Jul 12, Jul 19, Jul 26, Aug 2, Aug 9, Aug 16, Aug 23, Aug 30, Sep 6, Sep 13, Sep 20, Sep 27, Oct 4, Oct 11, Oct 18, Oct 25, Nov 1, Nov 8, Nov 15, Nov 22, Nov 29, Dec 6, Dec 13, Dec 20, Dec 27, Jan 3, Jan 10, Jan 17, Jan 24, Jan 31, Feb 7, Feb 14, Feb 21, Feb 28, Mar 7, Mar 14, Mar 21, Mar 28
2	→	Mobilization, Survey, Layout	10 days	Wed 7/15/20	Tue 7/28/20			
3	→	Clearing and Grubbing	15 days	Wed 7/29/20	Tue 8/18/20	2		
4	→	Waterline Relocation	40 days	Wed 8/19/20	Tue 10/13/20	3		
5	→	Stormwater Reconfiguration	40 days	Wed 10/14/20	Tue 12/8/20	4		
6	→	Roadway Reconfiguration, Stabilization, and Base	40 days	Wed 12/9/20	Tue 2/2/21	5		
7	→	Paving, Signage, and Clean-up	13 days	Wed 2/3/21	Fri 2/19/21	6		
8	★	Substantial Completion	22 days	Sun 2/21/21	Mon 3/22/21			
9	→	Punch List Items	21 days	Mon 2/22/21	Mon 3/22/21			
10	→	Final Completion	0 days	Mon 3/22/21	Mon 3/22/21			

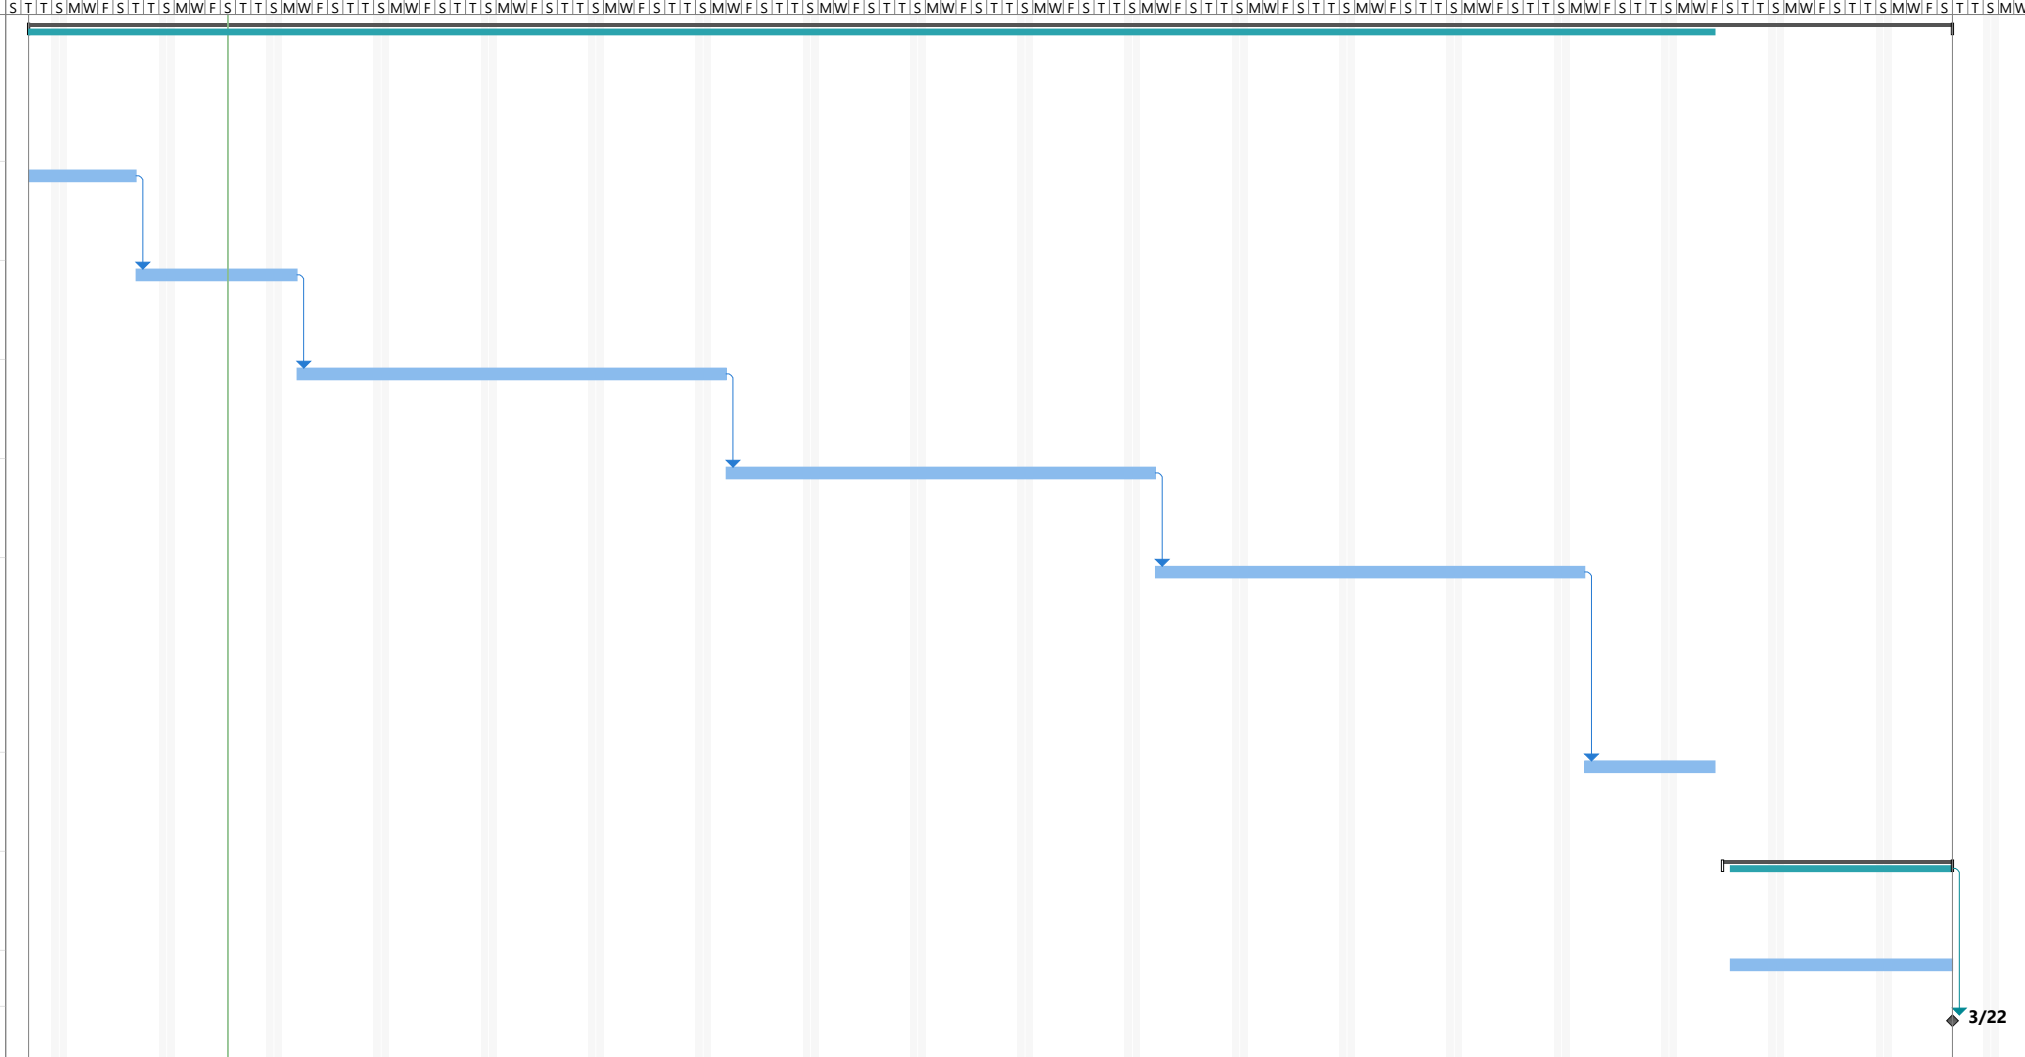

Project: Esc. Co. Ashcraft DRP
Date: Mon 8/10/20

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Manual Progress
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Progress	Progress
