


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		<b>Notice to Proceed/Paving Schedule</b>	<b>148 days</b>	<b>Thu 5/7/20</b>	<b>Sun 11/29/20</b>		
2		Mobilization, Planning, Weather Delay	50 days	Thu 5/7/20	Wed 7/15/20		
3		Milling and Initial Lift	10 days	Thu 7/16/20	Wed 7/29/20	2	
4		Excavation, Final Grading, and Dressing	20 days	Thu 7/30/20	Wed 8/26/20	3	
5		Final Lift and Final Markings	15 days	Thu 8/27/20	Wed 9/16/20	4	
6		<b>Substantial Completion</b>	<b>22 days</b>	<b>Sat 10/31/20</b>	<b>Sun 11/29/20</b>		
7		Punch List Items	20 days	Mon 11/2/20	Fri 11/27/20		
8		<b>Final Completion</b>	0 days	<b>Sun 11/29/20</b>	<b>Sun 11/29/20</b>		

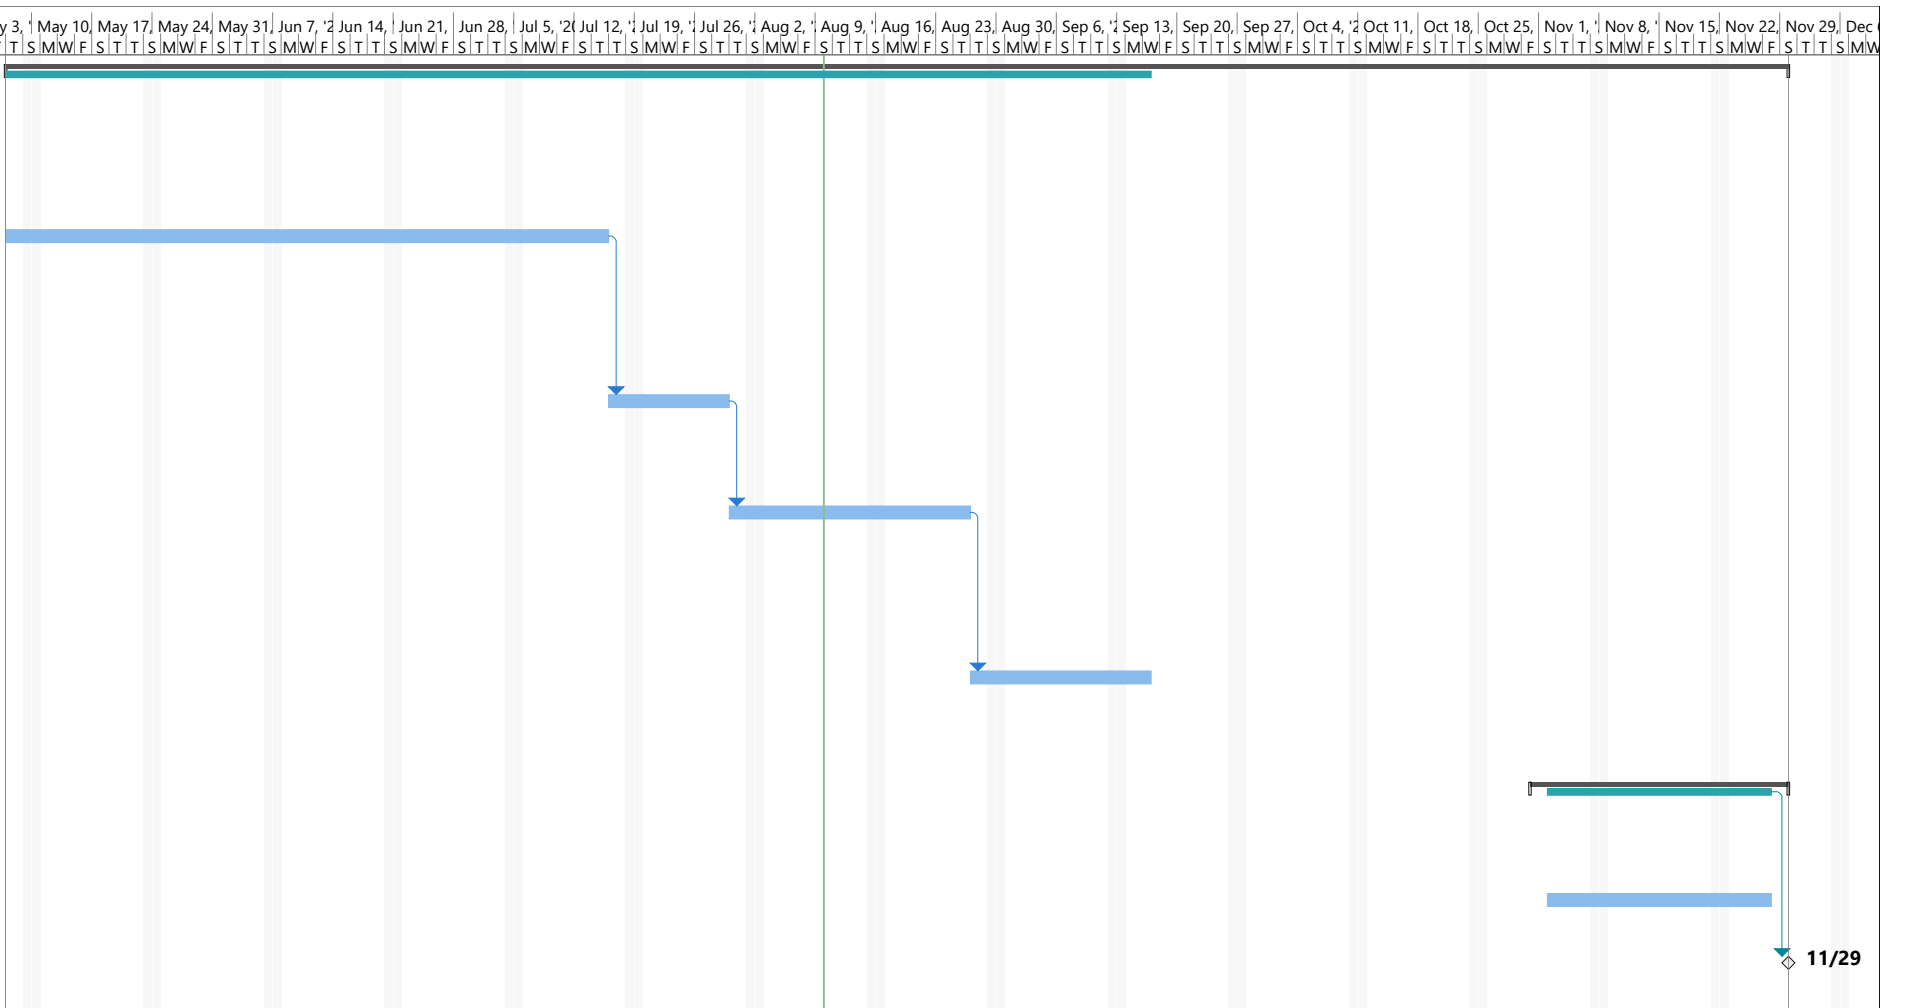

Project: Muscogee Rd. Resurfac  
Date: Mon 8/10/20

	Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress
	Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress
	Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress		Manual Progress
