


ID		Task Mode	Task Name	Duration	Start	Finish
1			Floridian Ditch Phase II Restoration (Sarasota Project)	301 days	Mon 7/27/20	Mon 9/20/21
2			NTP/Kick-off Meeting	1 day	Mon 7/27/20	Mon 7/27/20
3			Review Survey and update	7 days	Tue 7/28/20	Wed 8/5/20
4			Task 1 - Wetland Delineation	5 days	Tue 7/28/20	Mon 8/3/20
5			Wetland Delineation	5 days	Tue 7/28/20	Mon 8/3/20
6			Task 2 - Engineering Design and Construction Plan Development	87 days	Tue 8/4/20	Wed 12/2/20
7			Site, Stormwater, and Structural Design	30 days	Tue 8/4/20	Mon 9/14/20
8			Prepare Line and Grade Drawings	7 days	Tue 9/15/20	Wed 9/23/20
9			60% Line and Grade Review Meeting	1 day	Thu 9/24/20	Thu 9/24/20
10			Address 60% Line and Grade Meeting Comments	1 day	Fri 9/25/20	Fri 9/25/20
11			Develop and Prepare 100% Design, Plans, Specifications	30 days	Mon 9/28/20	Fri 11/6/20
12			100% MM QC	3 days	Mon 11/9/20	Wed 11/11/20
13			Submit 100% Construction Plans and Specs	1 day	Thu 11/12/20	Thu 11/12/20
14			100% County Review	7 days	Fri 11/13/20	Mon 11/23/20
15			Address 100% Comments and Submit Plans	7 days	Tue 11/24/20	Wed 12/2/20
16			Task 3 - Permitting and/or Regulatory Coordination	45 days	Mon 11/9/20	Fri 1/8/21
17			Prepare, Submit, and Receive NFWFMD Permit	45 days	Mon 11/9/20	Fri 1/8/21
18			Prepare, Submit, and Receive FDOT Permit	45 days	Mon 11/9/20	Fri 1/8/21
19			Task 4 - Bidding Assistance	60 days	Mon 1/11/21	Fri 4/2/21
20			Pre-Bid Meeting, Address Comments, & Award Project	60 days	Mon 1/11/21	Fri 4/2/21
21			Task 5 - Limited Construction Administration	121 days	Mon 4/5/21	Mon 9/20/21
22			Pre-Construction Meeting	1 day	Mon 4/5/21	Mon 4/5/21
23			Construction	120 days	Tue 4/6/21	Mon 9/20/21


Project: Schedule.mpp Date: Fri 7/31/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


Predecessors																													July													
	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S										
2																																										
2																																										
2																																										
5																																										
5																																										
7																																										
8																																										
9																																										
10																																										
11																																										
12																																										
13																																										
14																																										
11																																										
11																																										
11																																										
18																																										
18																																										
20																																										
20																																										
22																																										


Project: Schedule.mpp Date: Fri 7/31/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

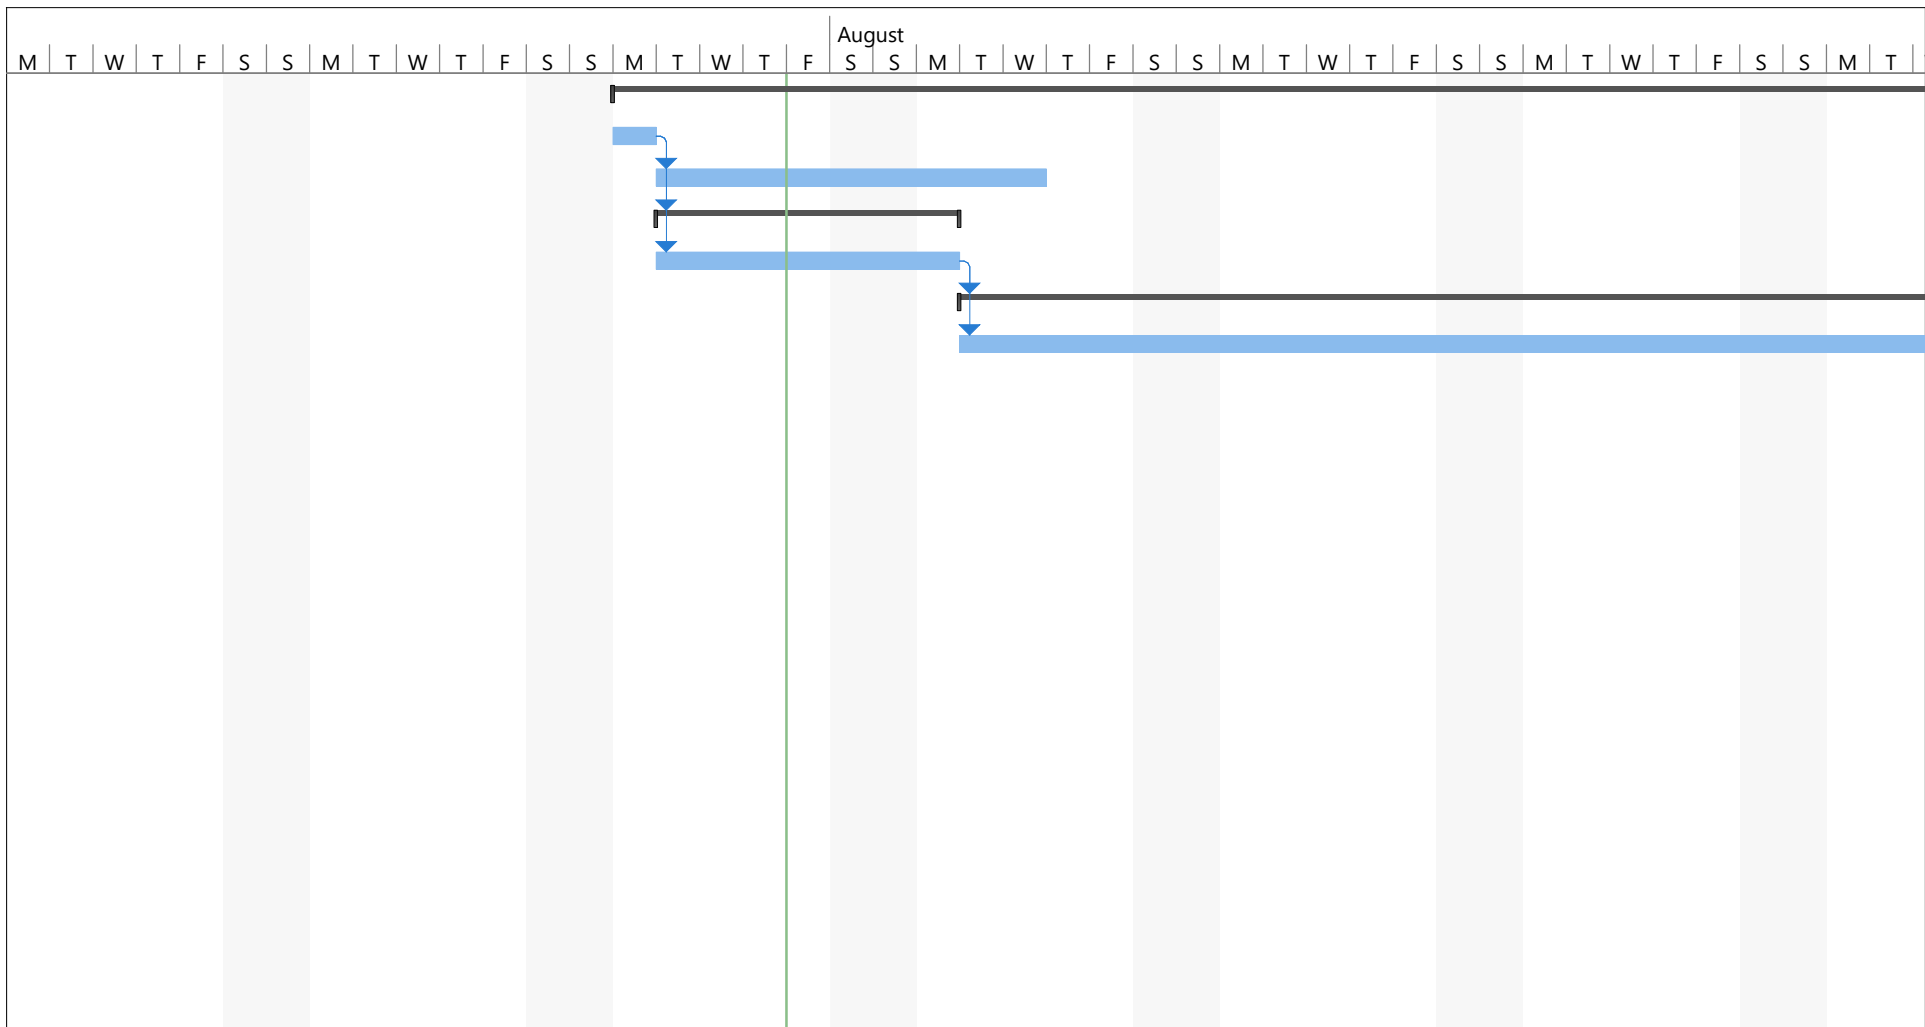



Project: Schedule.mpp Date: Fri 7/31/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

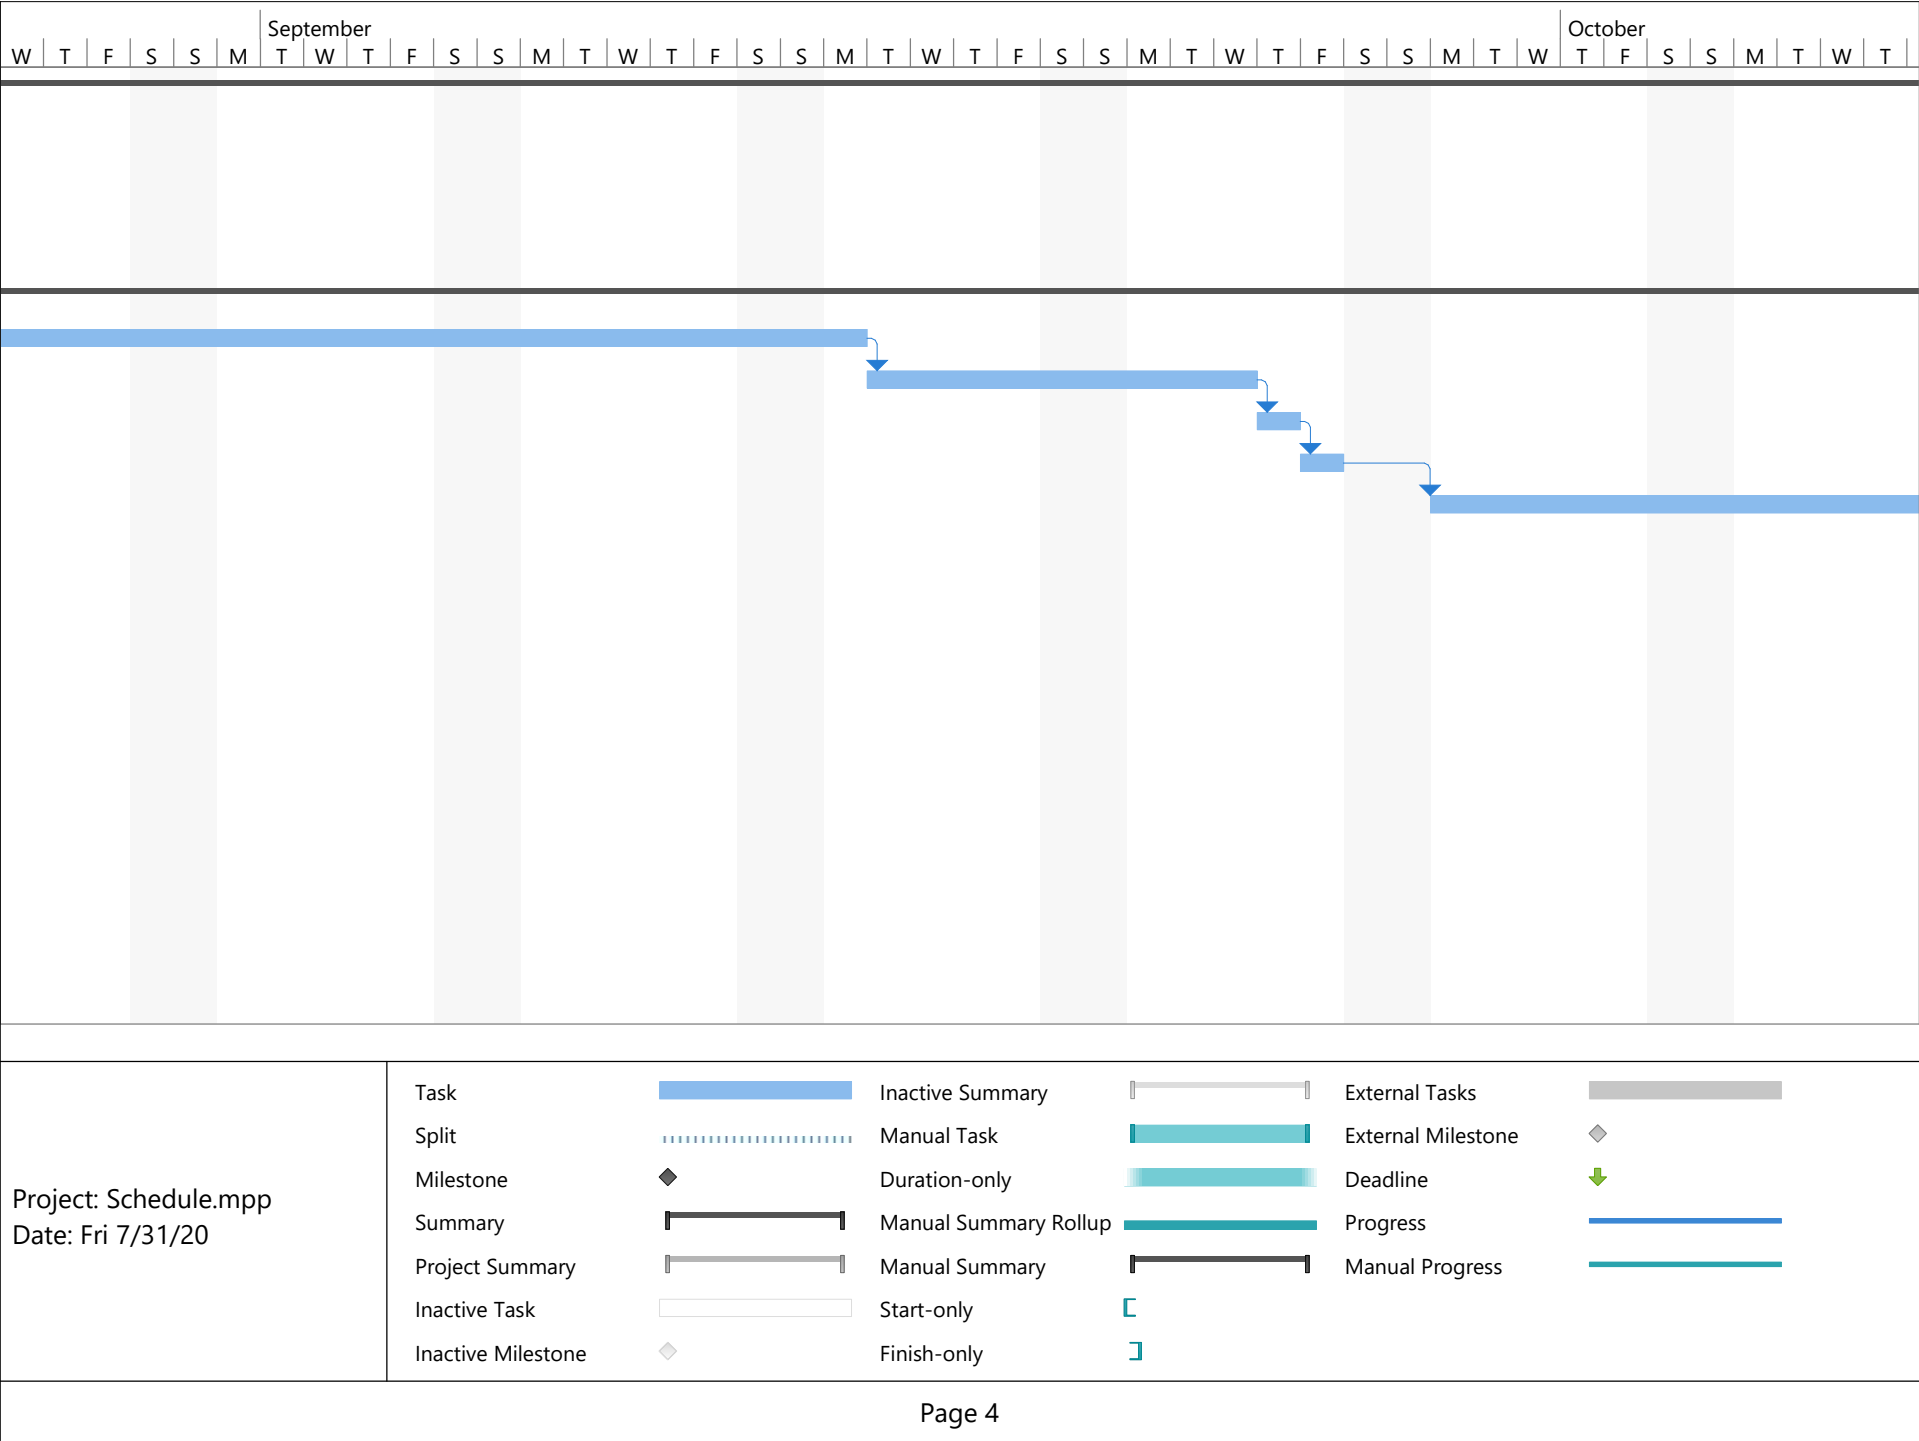

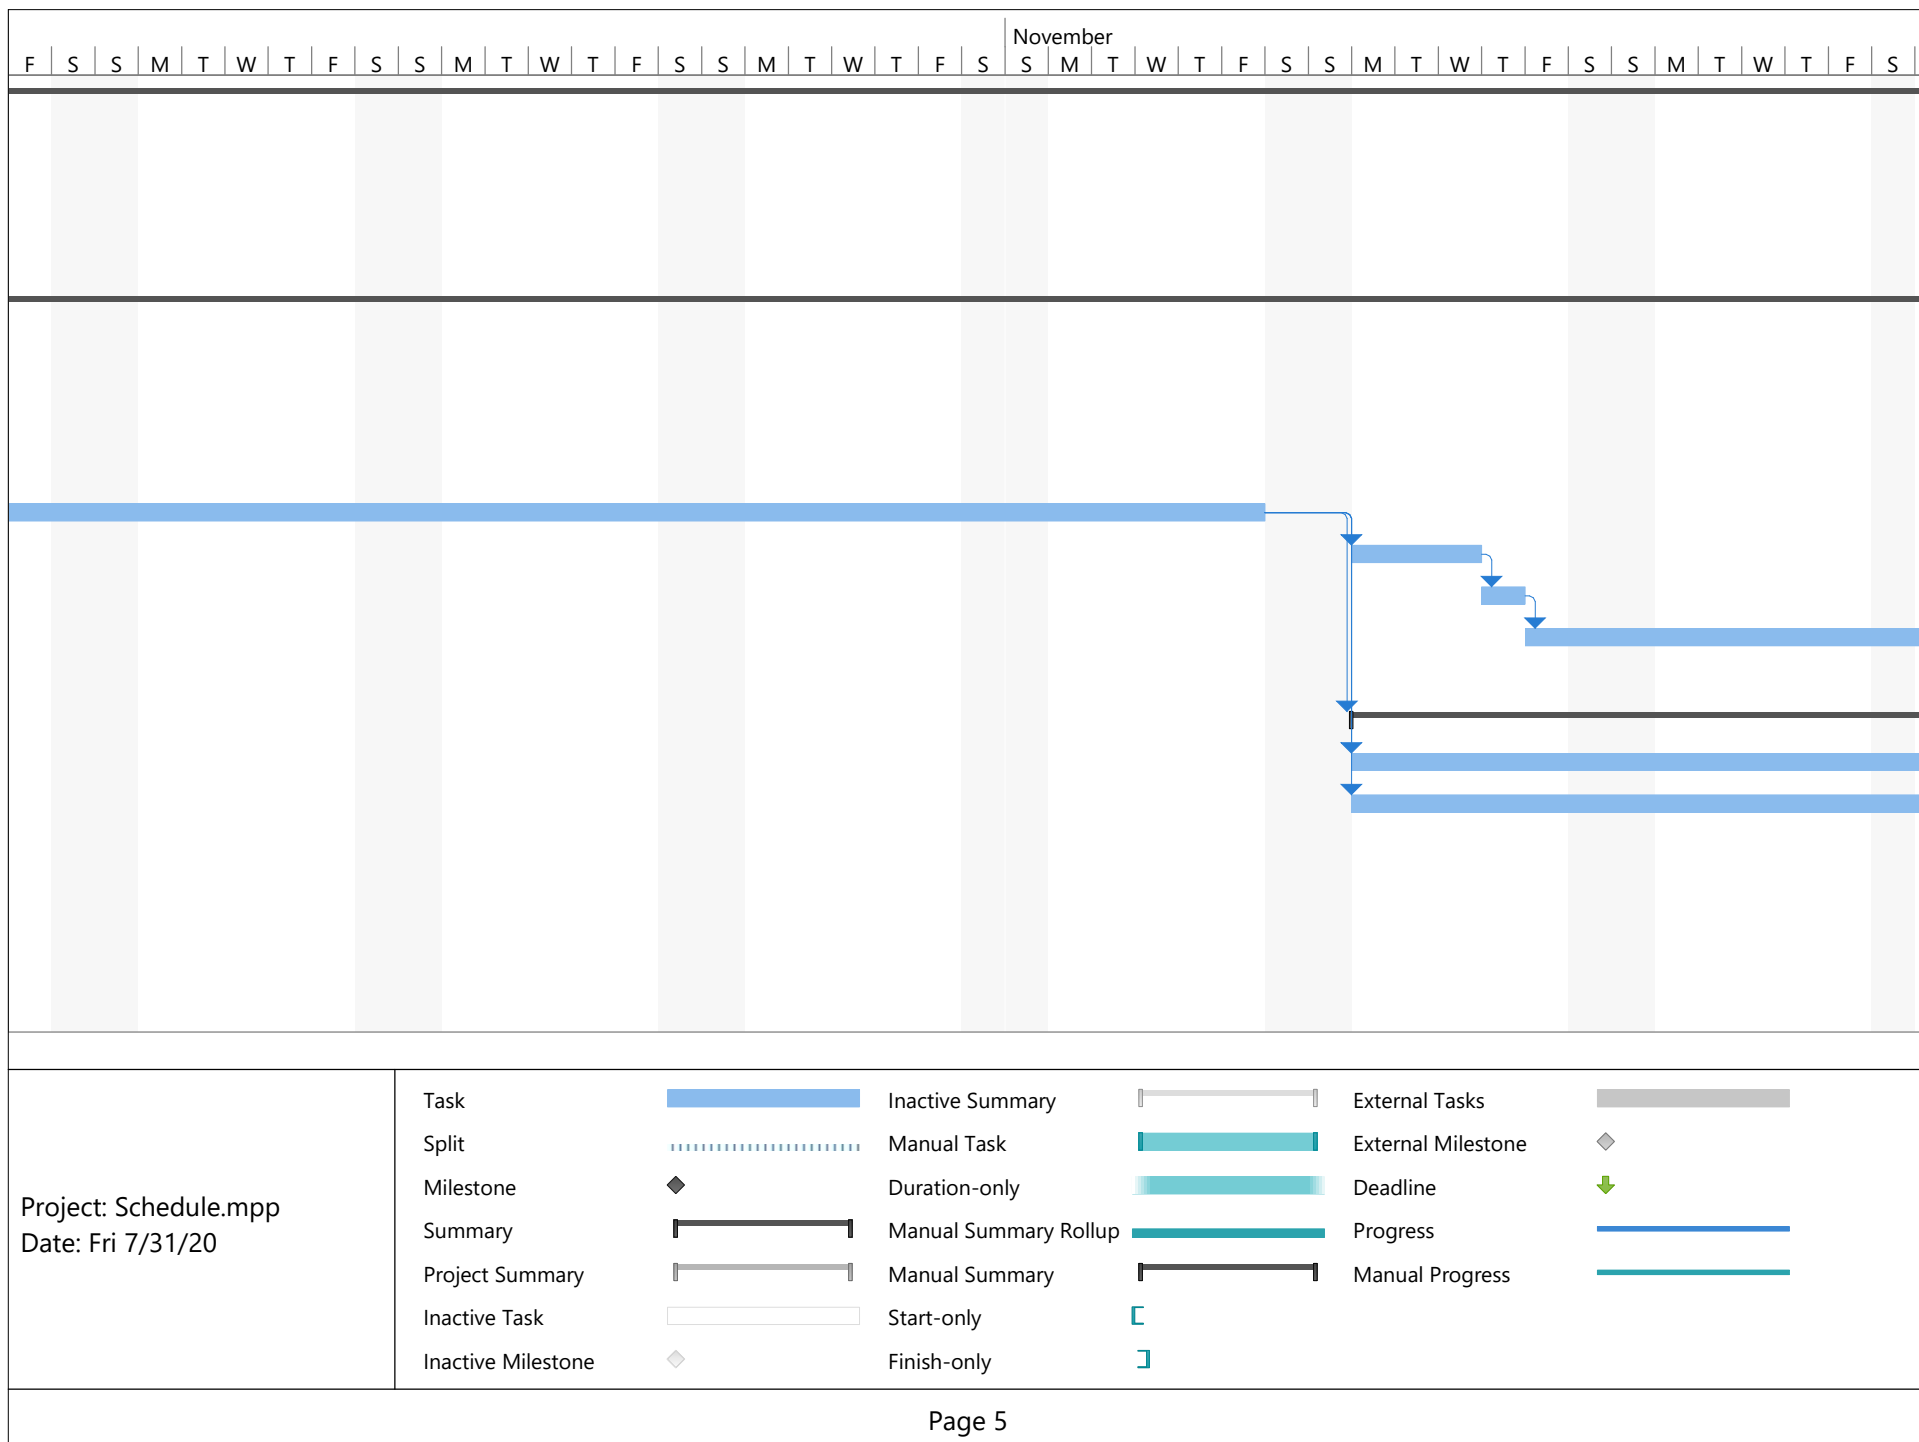


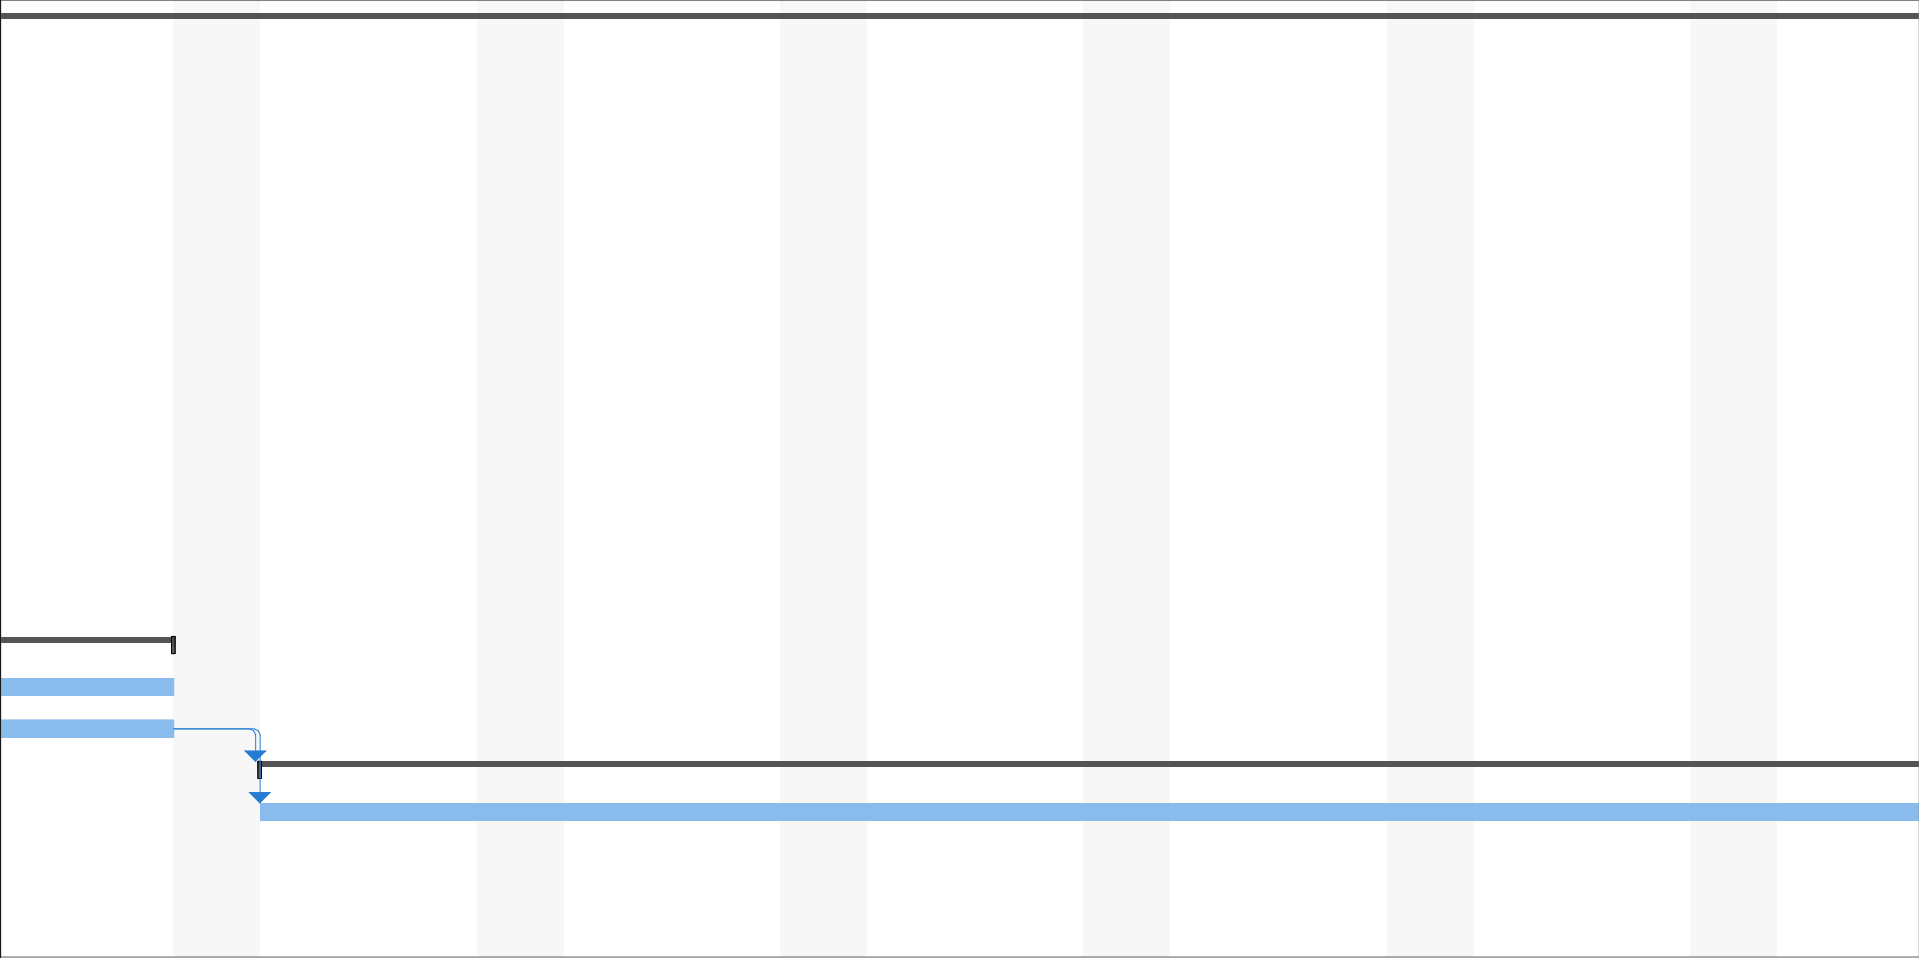

Project: Schedule.mpp Date: Fri 7/31/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

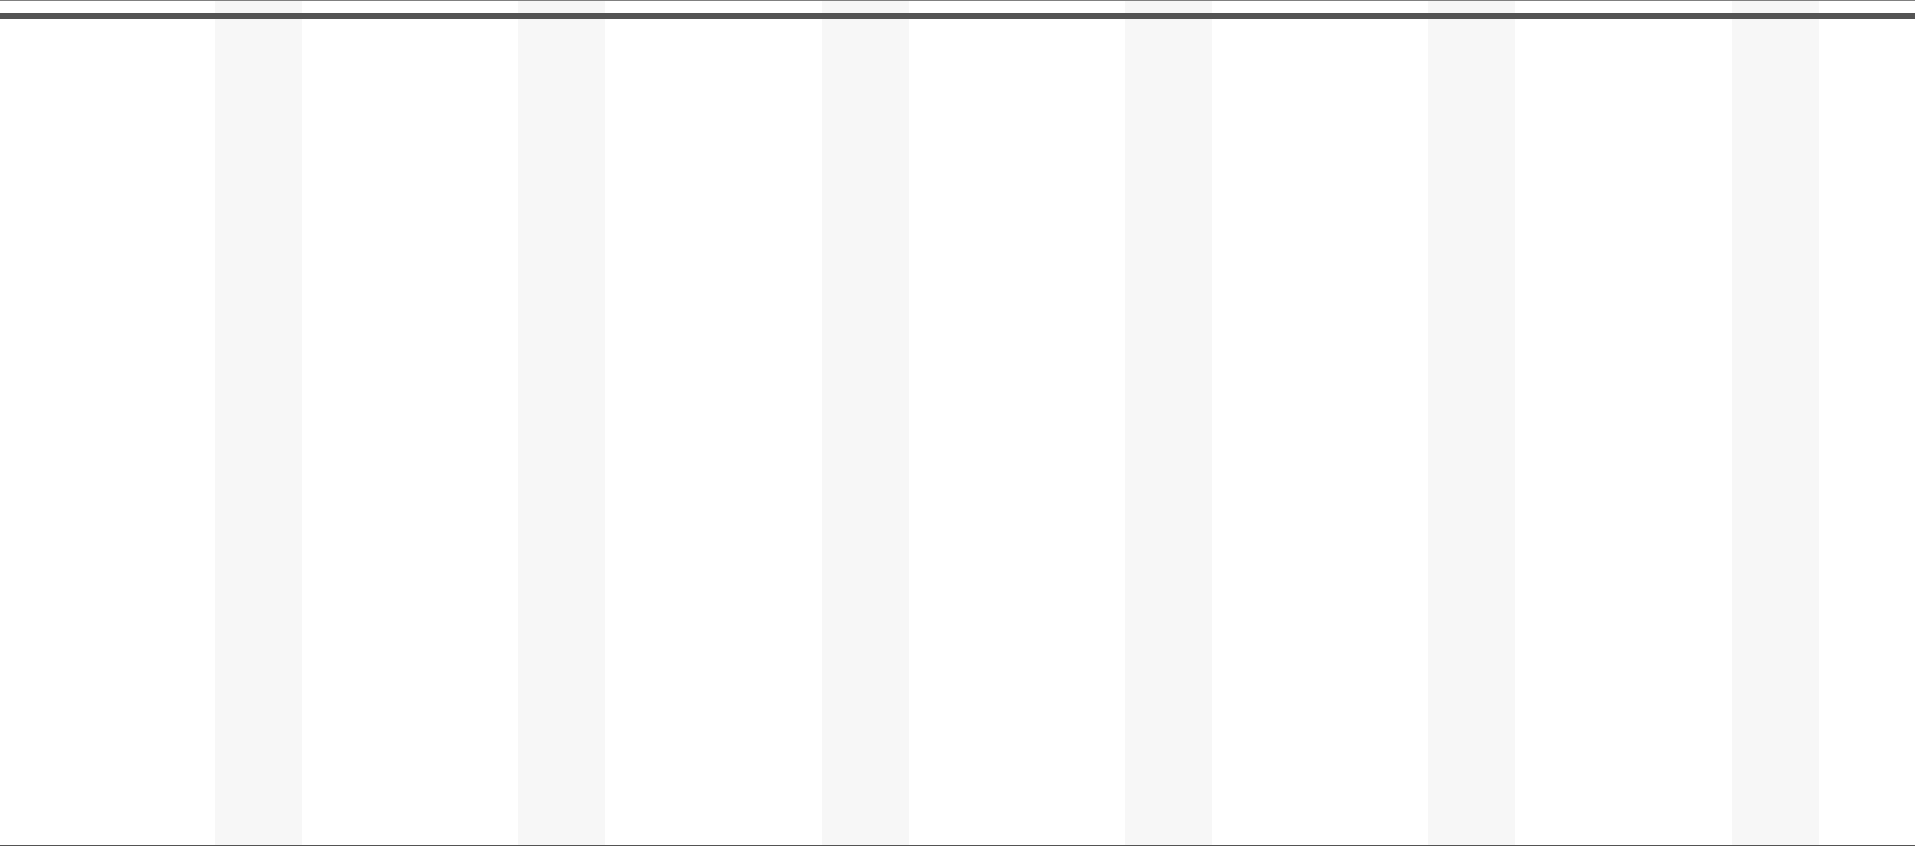

Project: Schedule.mpp Date: Fri 7/31/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

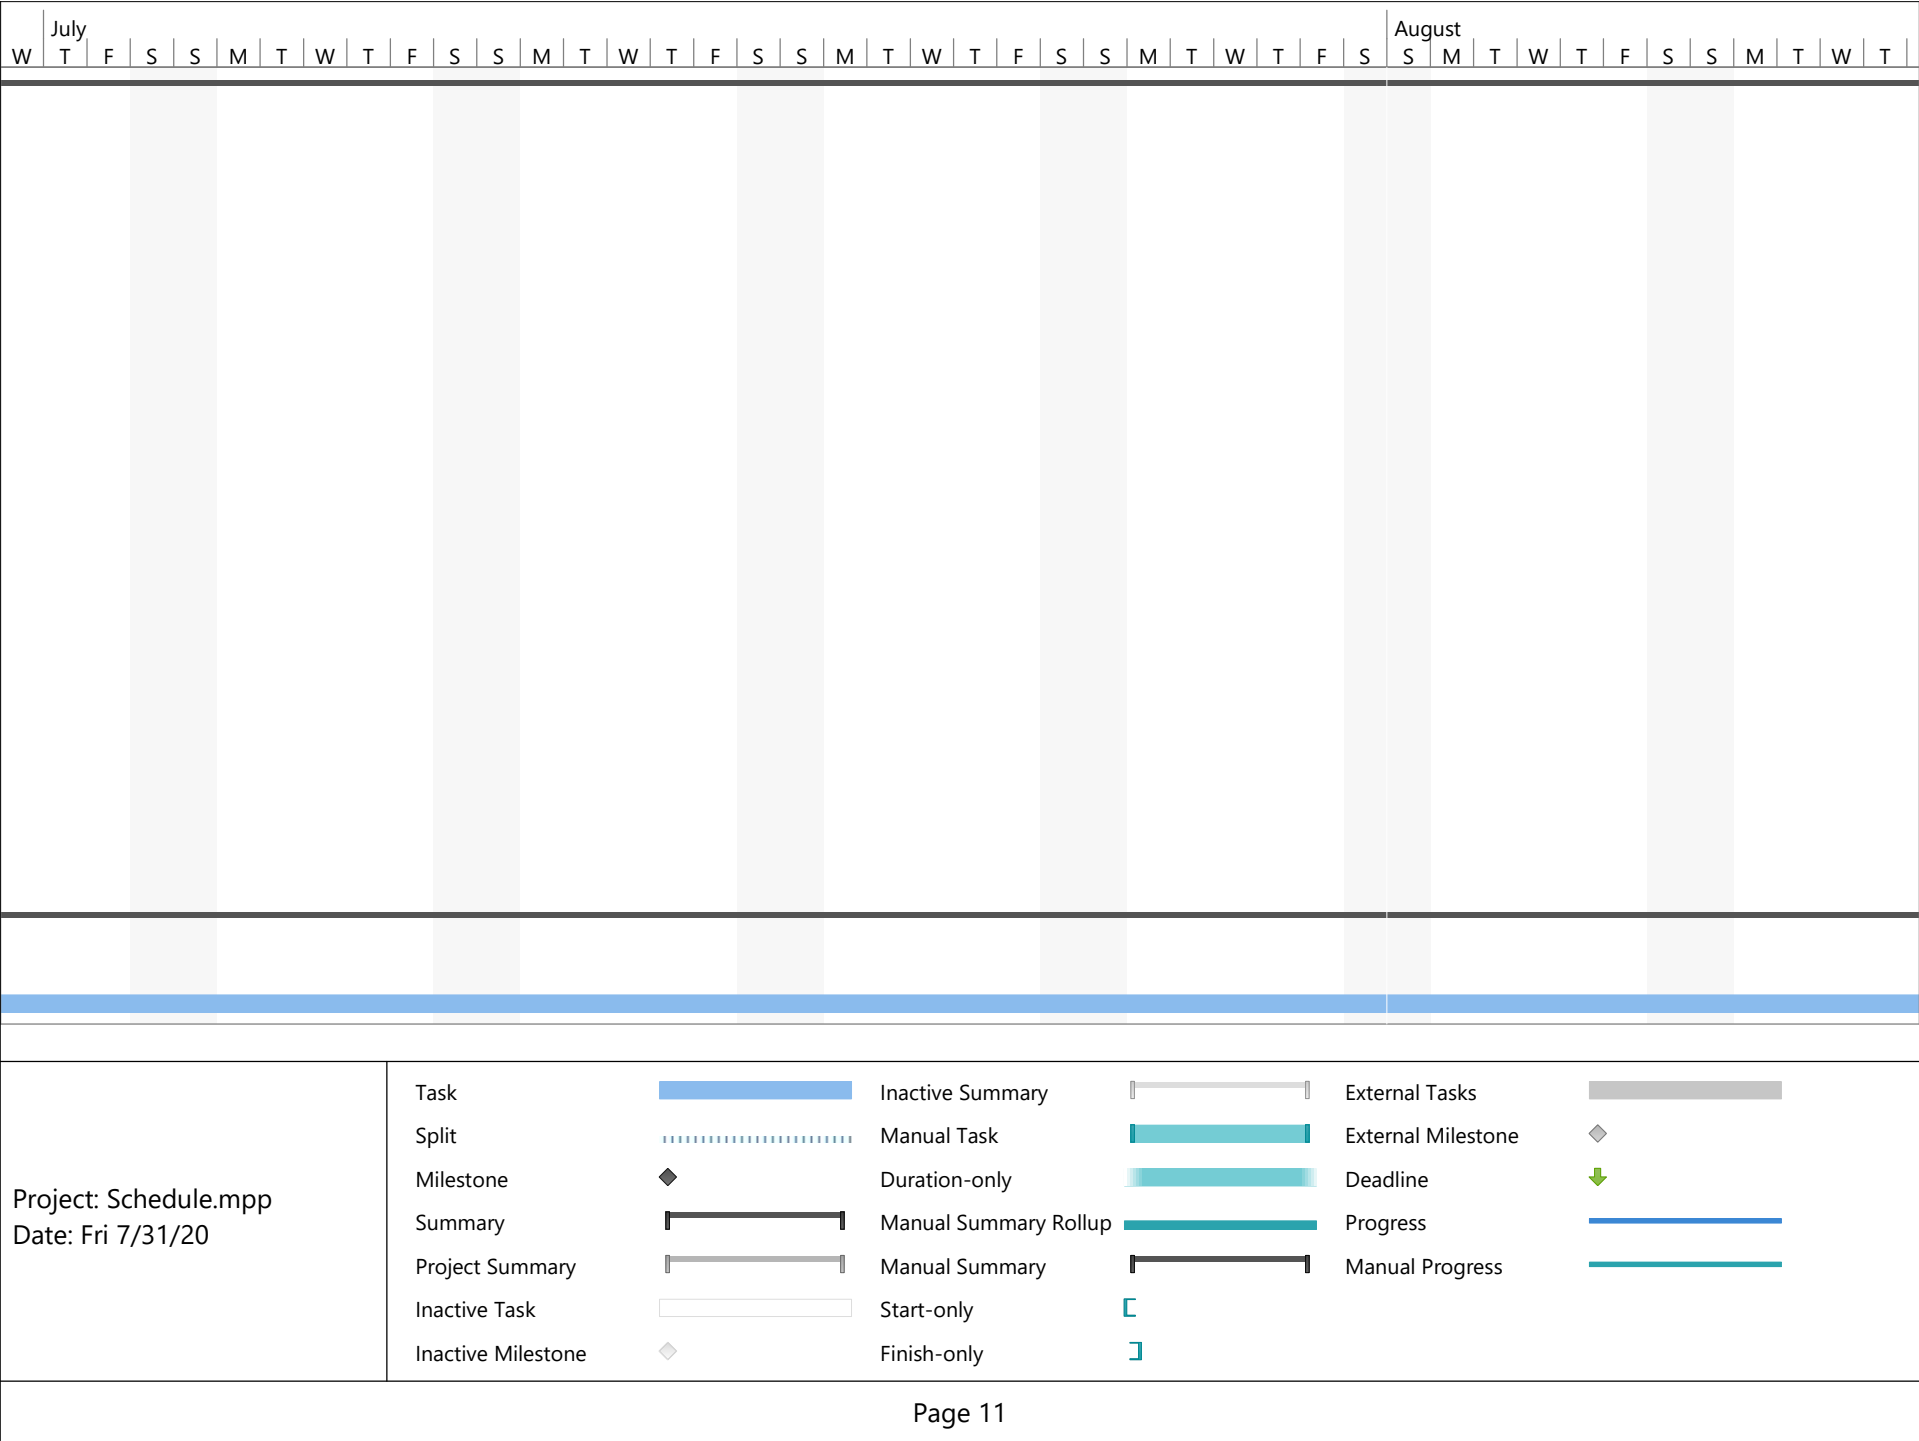

Project: Schedule.mpp
Date: Fri 7/31/20

