


Project Schedule  
West Detroit Blvd. Resurfacing  
August 2020

ID	Task Name	Duration	Start	Finish
1	Project Duration	453 days	Tue 8/11/20	Thu 5/5/22
2	Notice to Proceed	1 day	Tue 8/11/20	Tue 8/11/20

3	Data Collection	10 days	Wed 8/12/20	Wed 8/12/20
4	Review Existing Data	10 days	Wed 8/12/20	Wed 8/12/20
5	Field Reviews	5 days	Wed 8/12/20	Wed 8/12/20
6	Coordination with County and Property Owners	10 days	Wed 8/12/20	Wed 8/12/20
7	60% Detroit Blvd. Roadway Design Submittal	86 days	Wed 8/26/20	Wed 8/26/20
8	Prepare 60% Plans	45 days	Wed 8/26/20	Wed 8/26/20
9	Utility and Sub Coordination	15 days	Wed 8/26/20	Wed 8/26/20
10	QA/QC	10 days	Wed 10/28/20	Wed 10/28/20
11	Submit 60% Plans	1 day	Wed 11/11/20	Wed 11/11/20
12	Escambia County Review	30 days	Thu 11/12/20	Thu 11/12/20
13	100% Detroit Blvd. Roadway Design Submittal	91 days	Thu 12/24/20	Thu 12/24/20
14	Prepare 100% Plans and Specs	40 days	Thu 12/24/20	Thu 12/24/20
15	Utility and Sub Coordination	15 days	Thu 12/24/20	Thu 12/24/20
16	QA/QC	10 days	Thu 2/18/21	Thu 2/18/21
17	Submit 100% Plans and Specs	1 day	Thu 3/4/21	Thu 3/4/21
18	Escambia County Review	30 days	Fri 3/5/21	Fri 3/5/21
19	Finalize Plans and Specs	10 days	Fri 4/16/21	Fri 4/16/21
20	Package to Purchasing	79 days	Fri 4/30/21	Fri 4/30/21
21	Prepare Bid Package	5 days	Fri 4/30/21	Fri 4/30/21
22	Advertise	30 days	Fri 5/7/21	Fri 5/7/21
23	Pre Bid Meeting	1 day	Fri 6/18/21	Fri 6/18/21
24	Bid Opening Meeting	10 days	Mon 6/21/21	Mon 6/21/21
25	Review and Finalize Bid Tabulation	3 days	Mon 7/5/21	Mon 7/5/21
26	BCC Award	30 days	Thu 7/8/21	Thu 7/8/21
27	Construction Duration and Assistance	186 days	Thu 8/19/21	Thu 8/19/21
28	Pre Construction Meeting	1 day	Thu 8/19/21	Thu 8/19/21
29	Construction NTP	5 days	Fri 8/20/21	Fri 8/20/21
30	Construction Days	180 days	Fri 8/27/21	Thu 5/5/22

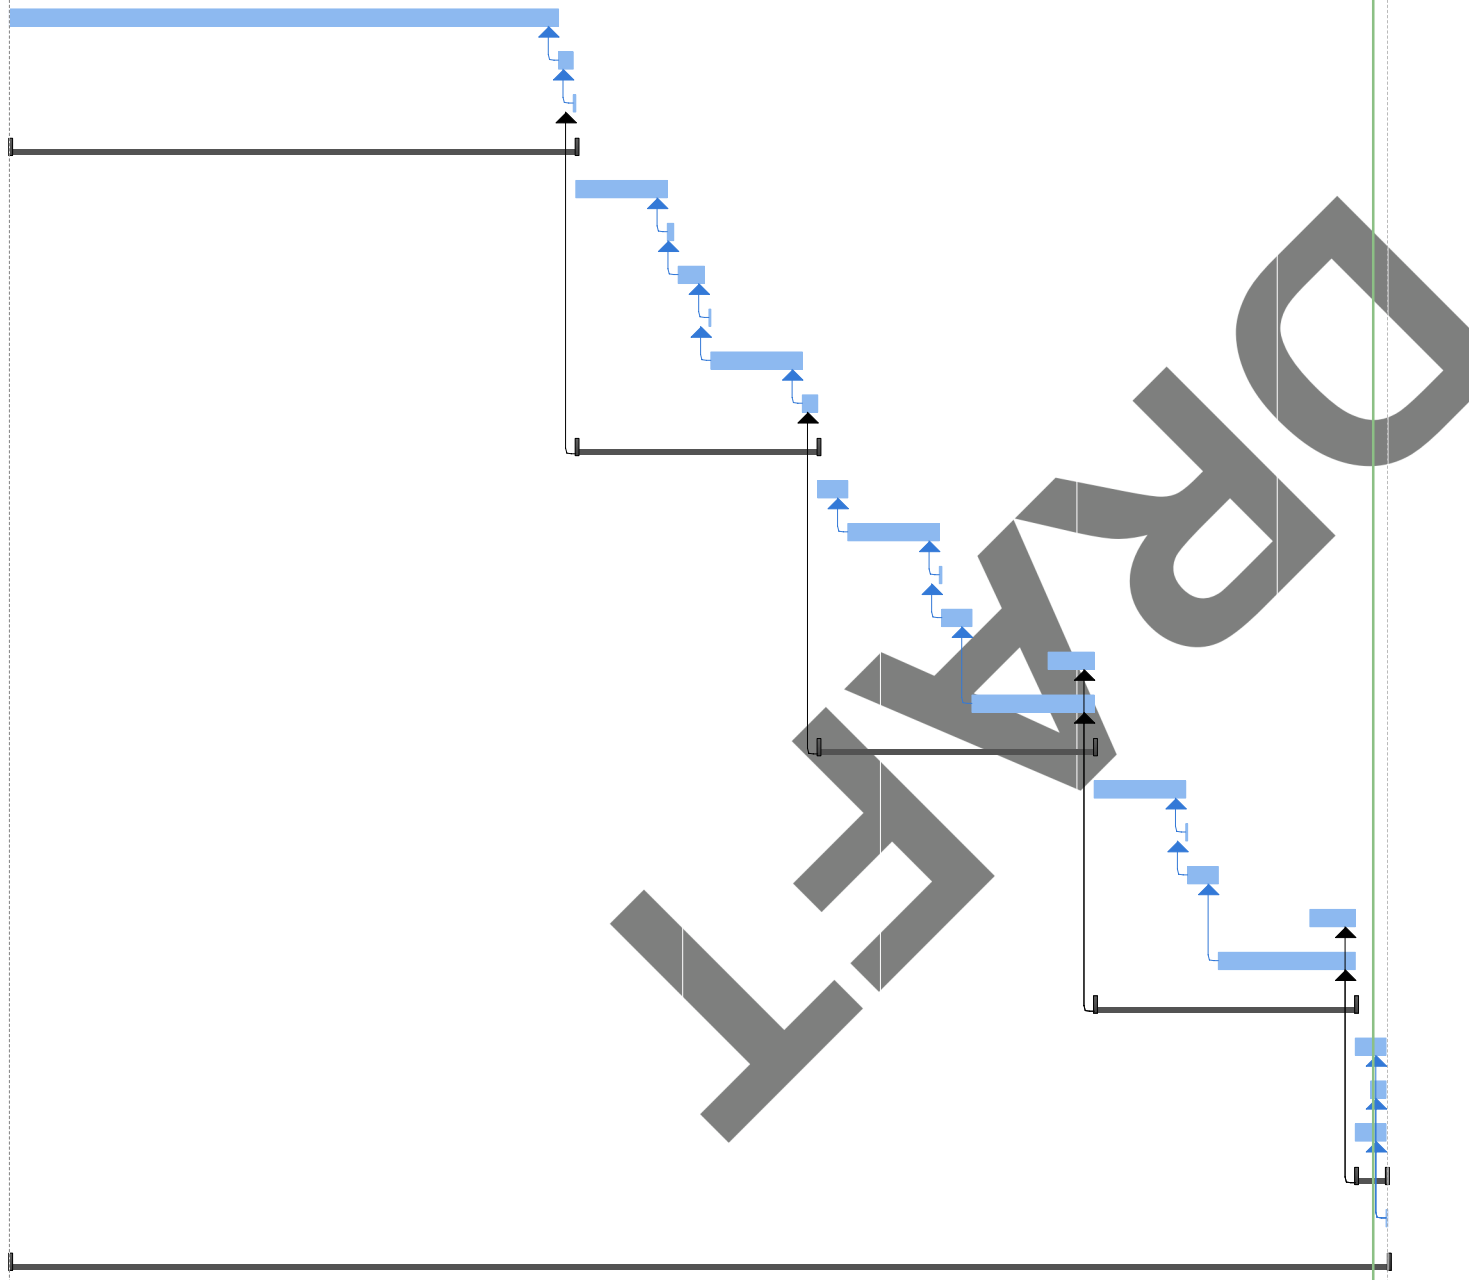

Project: West Detroit Blvd.  
Date: Tue 8/18/20

Task	Project Summary	Inactive Task	Manual Task	Start-only	Finish-only	External Tasks	Manual Progress	Deadline
Task	Project Summary	Inactive Task	Manual Task	Start-only	Finish-only	External Tasks	Manual Progress	Deadline
Milestone	Inactive Milestone	Inactive Milestone	Manual Summary Rollup	External Milestone	External Milestone	Manual Summary	Manual Progress	Deadline
Summary	Summary	Summary	Manual Summary	External Milestone	External Milestone	Manual Summary	Manual Progress	Deadline
